Reclaim Revalue Reframe
training programme

Building Capacity for Waste Picker Integration

Piloting the South Africa Waste Picker Registration System (SAWPRS)



Prepared by:

Prof Melanie Samson (University of Johannesburg)

Andries Mkhatshwa, Nomcebo Dlamini and Jennifer van den Bussche (Sticky Situations)

Submitted – August 15, 2022

cITIES SUPPORT PROGRAMME · STICKY SITUATIONS · UNIVERSITY OF THE WITWATERSRAND JOHANNESBURG · CSIR · UNIDO UNITED NATIONS INDUSTRIAL DEVELOPMENT ORGANIZATION

Overview


PART 1	Background
PART 2	Overview of Pilot Project
PART 3	System Design
PART 4	Pilot Sites
PART 5	Outcomes
PART 6	Lessons
PART 7	Recommendations

PART 1

Background

Background – The need for Registration

- Need identified during development of Waste Picker Integration Guideline (2016-2019)
- Need heightened during COVID-19 lockdowns (2020)
- UNEP Waste Rapid Response Project: agreed core questions and approach, concept note by Prof Linda Godfrey (2020-2021)
- EPR Regulations – PROs must pay waste pickers registered on the national system for services provided

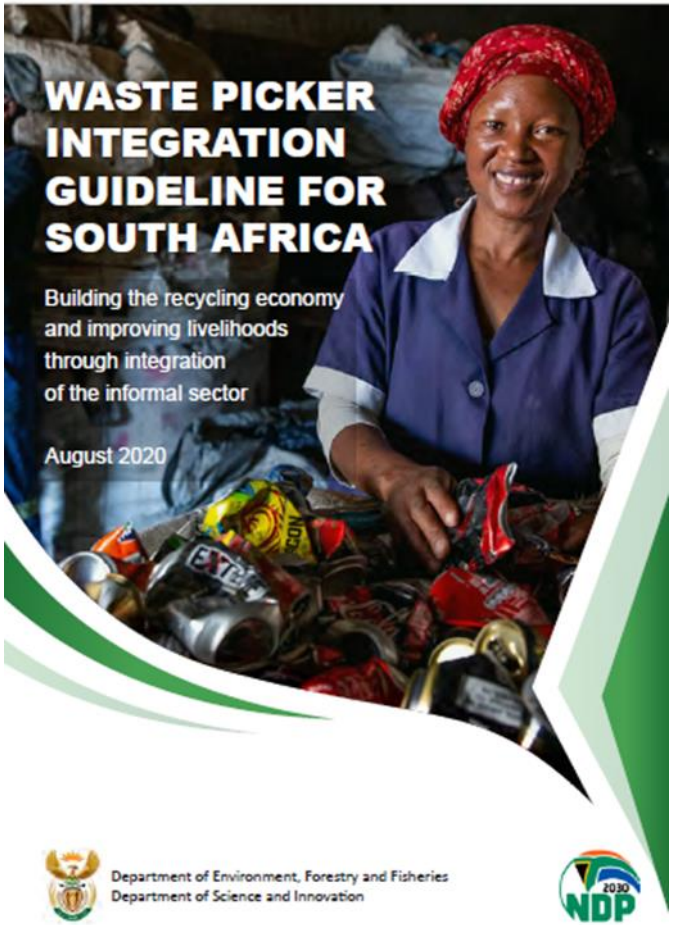

Reclaim Revalue Reframe training programme

Building Capacity for Waste Picker Integration

PART 2

Overview of the pilot project

Pilot Project - Partners and Principles

Partners

- Funded by CSP, DSI and UNIDO
- Partnership between CSI and Wits/UJ
- Sticky Situations pilot implementing agent
- All key stakeholders – waste picker organisations' national, provincial and local government; industry associations/PROs, NGOs + academics

Principles

- Comply with 10 Waste Picker Integration Principles
- Reclaimer/Waste Picker led
- Part of meaningful integration in municipalities
- Municipal involvement
- All reclaimers registered (including non-SA)
- Only essential data collected

Reclaim Revalue Reframe training programme

Building Capacity for Waste Picker Integration

Pilot Project - Methodology

- Stakeholder meeting
- 4 sites – ARO, SAWPA, Cape Town, BCMM
- Participatory development of wireframe and online system with CSIR and TAG
- Piloting in each site
- Waste pickers who already piloted went to other sites to do outreach and support pilot



Registration in Cape Town

Reclaim Revalue Reframe training programme

Building Capacity for Waste Picker Integration

Pilot Project – Piloting Phases

1. Partnership
2. Education
3. Planning
4. Initial outreach & wp engagement
5. 1 week mobilization just prior to pilot week
6. Pilot week
    1. 1 day training
    2. 3 days piloting
    3. 1 day evaluation
7. Card distribution




Registration at Msunduzi landfill

Reclaim Revalue Reframe training programme

Building Capacity for Waste Picker Integration

PART 3

System design

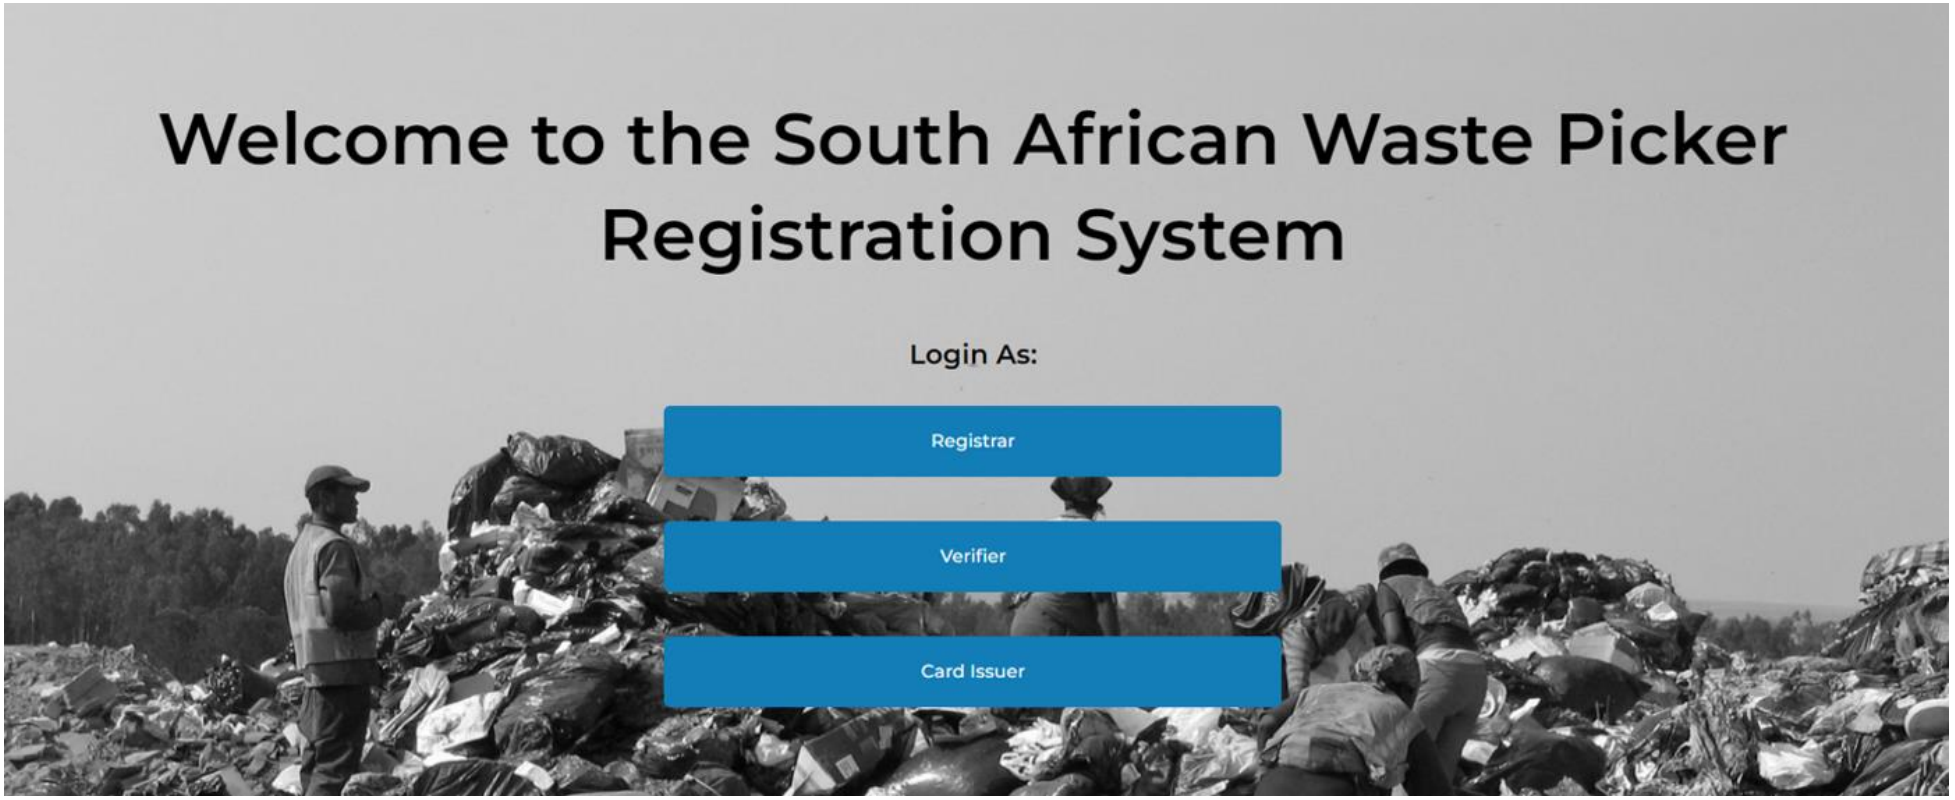

- Participatory system design
- Online open stakeholder meeting
- Technical Advisory Group
- Designed by CSIR

Reclaim Revalue Reframe
training programme

Building Capacity for Waste Picker Integration

PART 4

Pilot sites

ARO - Johannesburg

- **Partner** – African Reclaimers Organisation
- **Dates** – Feb 14 – 19, 2022
- **Pilot locations** - Marie Louise Landfill, Johannesburg CBD and Alexandra Township
- **# registered and verified** – 226



Registering a reclaimer

Reclaim Revalue Reframe training programme

Building Capacity for Waste Picker Integration

SAWPA Pietermaritzburg

- **Partner** – South African Waste Pickers Association
- **Dates** – Feb 29 – March 2, 2022
- **Pilot locations** – Msunduzi Landfill
- **# registered and verified** – 256



Taking photos for ID cards

Reclaim Revalue Reframe training programme

Building Capacity for Waste Picker Integration

City of Cape Town

- **Partners** – City of Cape Town and ARO
- **Dates** – March 14 – 18, 2022
- **Pilot locations** – Retreat, Khayelitsha, Pinelands
- **# registered and verified** – 381 (327 during registration + 54 during card distribution)



Distribution of cards in retreat

Reclaim Revalue Reframe training programme

Building Capacity for Waste Picker Integration

Buffalo City Metropolitan Municipality

- **Partner** – BCMM, ARO & SAWPA
- **Dates** – May 23 – 27, 2022
- **Pilot locations** – Berlin Landfill, Merrifield, Southernwood
- **# registered and verified** – 131



Registration of reclaimers at Merrifield

Reclaim Revalue Reframe
training programme

Building Capacity for Waste Picker Integration

PART 5

Outcomes

Outcomes

994 waste pickers registered in 4 pilot sites

- Pilot successfully completed in all four pilot sites.
- 25 waste pickers trained as registrars and verifiers (18 female and 7 male)
- Increased capacity of trained waste pickers + organisations
- Educated more than 1000 waste pickers on integration, registration and EPR
- Deepened municipal understanding of integration
- Forged relationships for integration
- Finalised online system
- Established registration methodology

Reclaim Revalue Reframe training programme

Building Capacity for Waste Picker Integration

PART 6

Lessons

Lessons

- Education and training of municipal officials is crucial
- Municipal officials have limited time to do registration.
- But engagement is key
- Outreach by waste pickers is crucial
- Previous municipal registrations created distrust
- Waste pickers must lead – trust and expertise
- Provides basis for waste picker integration
- Need stakeholder steering committee



Reclaim Revalue Reframe
training programme

Building Capacity for Waste Picker Integration

PART 7

Recommendations

Recommendations



1. Development of a SAWPRS app
2. Partnership approach and reclaimer leadership should be continued in co-governance integration committees, incl in EPR.
3. Launch National Waste Picker Registration Campaign
4. Development of EPR waste picker payment system informed by lessons and rooted in participation and co-governance.
5. Decisions on long-term hosting and governance of SAWPRS required

Reclaim Revalue Reframe
training programme

Building Capacity for Waste Picker Integration

Thank you

Contacts:

Melanie Samson
Email: melanies@uj.ac.za
Cell: +27 (0)78 800 4358

Andries Mkhatshwa
Email: andries@stickysituations.org
Cell: +27 (0)76 779 3704

Reclaim Revalue Reframe training programme

Building Capacity for Waste Picker Integration
